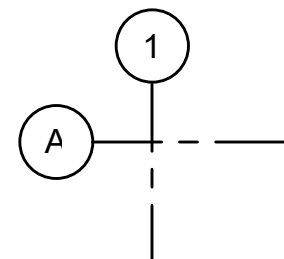




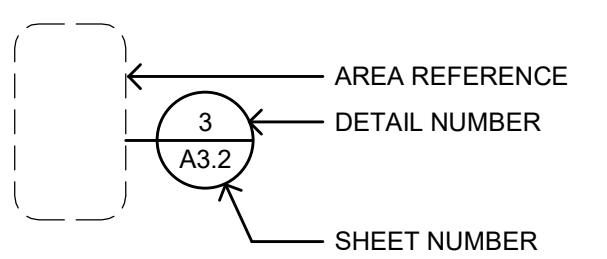
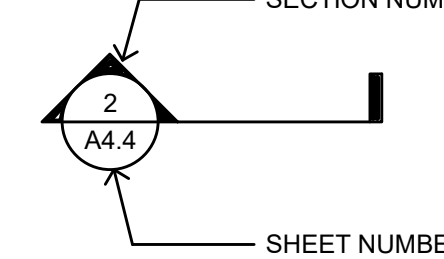







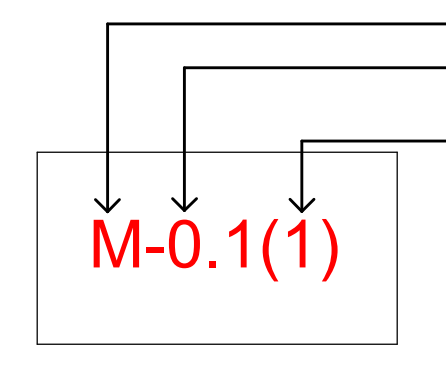


BUILDING GRID LINES	REVISION CLOUD (CLOUD AROUND REVISION OPTIONAL)
	
WINDOW SYMBOL	ROOM LABEL
	
DOOR SYMBOL	
	
DETAIL	SECTION
	
EXTERIOR ELEVATION	INTERIOR ELEVATION
	
EQUIPMENT TAG	MATERIAL TAG
	
DIMENSION STRING	NORTH ARROW
	
WORK POINT OR CONTROL POINT	SHEET KEY
	
SYMBOL LEGEND NO SCALE	RESUME OF WORK OWNER/LOCAL GC - ON SITE WORK: POST-DELIVERY NO SCALE

DIMENSIONING NOTES	RESUME OF WORK OWNER/LOCAL GC - ON SITE WORK: PRE-DELIVERY NO SCALE
1. ALL DIMENSIONS ARE TO FACE OF STRUCTURE (F.O.S.) UNLESS OTHERWISE NOTED. SHEATHING IS NOT INCLUDED AS STRUCTURE IN DIMENSIONING. DIMENSIONS ARE TO FRAMING.	
2. DO NOT SCALE FROM DRAWINGS.	
3. ANY INCONSISTENCIES OR UNFORESEEN CONDITIONS TO BE REVIEWED BY HOME EC PRIOR TO PROCEEDING WITH CONSTRUCTION.	
4. ALL CASEWORK DIMENSIONS TO FACE OF FINISH.	
MISCELLANEOUS NOTES	
5. SOUND INSULATION REQUIRED IN ALL INTERIOR WALLS.	
6. PROVIDE 1.28 GALLONS OF WATER PER FLUSH TOILETS.	
7. WATER HEATERS SHALL BE STRAPPED OR HAVE A RIGID CONNECTION TO AN ADJACENT WALL.	
8. ALL INSULATION MATERIALS SHALL BE CERTIFIED BY THE MANUFACTURER AS COMPLYING WITH THE REQUIRED QUALITY STANDARDS FOR INSULATION MATERIAL.	
9. EXTERIOR DOORS MUST OPEN OVER A LANDING NOT MORE THAN 1/4" BELOW THE THRESHOLD. EXCEPTION: PROVIDING THE DOOR DOES NOT SWING OVER THE LANDING THE LANDING SHALL NOT BE MORE THAN 8" BELOW THE THRESHOLD.	
10. AS REQUIRED BY AGENCY, AN APPROVED SEISMIC SHUTOFF VALVE SHALL BE INSTALLED ON THE FUEL GAS LINE ON THE DOWNSTREAM SIDE OF THE UTILITY METER AND BE RIGIDLY CONNECTED TO THE EXTERIOR OF THE BUILDING OR STRUCTURE CONTAINING THE FUEL GAS PIPING.	
11. FOR TYPICAL MOUNTING HEIGHTS OF DOOR HARDWARE, ELECTRICAL DEVICES AND MECHANICAL CONTROLS SEE DETAIL 6/M-0.4(1) REFER TO DETAIL WHEN DIMENSIONS OF STATED ITEMS ARE NOT SHOWN IN ELEVATION.	
12. PROVIDE R-12 EXTERIOR BLANKET INSULATION FOR HOT WATER HEATER. R-3 INSULATION SHALL BE PROVIDED FOR THE FIRST FIVE FEET OF THE WATER HEATER UTILITY PIPE. ALL WATER HEATING AND SPACE CONDITIONING EQUIPMENT, SHOWER HEADS, AND FAUCETS SHALL BE C.E.C. CERTIFIED. ALL STEAM AND STEAM CONDENSATE RETURN PIPING AND ALL CONTINUOUSLY RE-CIRCULATING DOMESTIC HEATING OR HOT WATER PIPING SHALL BE INSULATED PER PLUMBING DIVISION.	
13. INSULATION VALUES SHALL BE AS FOLLOWS: ALL EXTERIOR WALLS = R-22 TAPERED ROOF INSULATION = MINIMUM R-40, MAXIMUM AT RIDGE LINE R-50 8.25" HIGH DENSITY BATT INSULATION IN FLOORS = R-30 INTERIOR BATH AND BEDROOM WALLS BATT INSULATION = R-13	
14. HANDRAILS AT STAIRS SHALL BE REQUIRED WHERE THERE ARE 4 OR MORE RISERS, AND NOT BE LESS THAN 34" NOR MORE THAN 38" ABOVE LANDINGS AND NOSINGS OF TREADS.	
15. GRIPS ON RAILS SHALL HAVE A 1 1/2" MINIMUM AND 2" MAXIMUM DIAMETER OR OFFER EQUIVALENT GRIPPING SURFACE.	
16. GUARDRAILS AND HANDRAILS SHALL BE STRONG ENOUGH TO RESIST A 200 POUND POINT LOAD IN ANY DIRECTION.	
17. A COMPREHENSIVE REVIEW OF THE ENERGY COMPLIANCE CALCULATION AND DETAILS BASED ON CLIMATE ZONE AND BUILDING ORIENTATION WILL BE CONDUCTED BY THE LOCAL ENFORCEMENT AGENCY.	
18. AN OPERATION AND MAINTENANCE MANUAL SHALL BE PROVIDED TO THE BUILDING OCCUPANT OR OWNER	
19. PURSUANT TO SECTION 19981 (C) OF THE HEALTH AND SAFETY CODE, NO FACTORY-BUILT HOUSING SHALL BE IN ANY WAY MODIFIED DURING INSTALLATION UNLESS APPROVAL FOR SUCH MODIFICATION IS FIRST OBTAINED FROM THE LOCAL ENFORCEMENT AGENCY	

#	Number Existing	CORR C.T. CTR CTSK C.W.	Corridor Ceramic Tile Center Countersunk Cold Water	F.A. F.D. FDN F.E. F.G. FIN FLR FLASH F.O.C. F.O.F. F.O.M. F.O.S. FR FTG FURR GA GALV G.I. GL GND GR GYP H B H.C. HCP HDWR HDWD H.M. HORIZ HT HVAC H.W.	Fire Alarm Floor Drain Foundation Fire Extinguisher Finish Grade Finish Floor Flashing Face of Finish Face of Concrete Face of Frame Face of Masonry Face of Structure Frame Foot or Feet Footing Furring or Furred Gauge Galvanized Galvanized Iron Glass or Glazing Ground Grade Gypsum High Hollow Core Hollow Core Handicapped Hardware Hardwood Hollow Metal Horizontal Height Heating, Ventilation and Air Conditioning Hot Water	I.D. INCL INSUL INT JST JNT KIT LAM LAV L.F. L.H. L.R. LT LVR MATL MAX MECH MEMB MET MFR MH MIN MIR MISC M.O. M.R. MUL	Inside Diameter Including Insulation Interior Joint Joint Kitchen Laminate Lavatory Left Feet Left Hand Living Room Light Louver Material Maximum Mechanical Membrane Metal Manufacture Manhole Minimum Mirror Miscellaneous Masonry Opening Moisture Resistant Mullion								
RESUME OF WORK FACTORY SCOPE OF WORK 1. Structural Steel Frames a) Weld and assemble steel frame b) Prep, prime and paint c) Install blocking and blocking fastener at steel beams d) Notes: Supply mating plates, bolts, and accessories to be installed in field 2. Floor Assembly a) Install floor joists b) Install insulation c) Install plywood subfloor d) Install tile flooring at bathroom locations e) Install stair and landing framing (for 2 story only) 3. Ceiling Assembly a) Install gypsum board ceiling, finish and paint b) Install ceiling joists at dropped ceiling locations c) Install exterior wood siding soffit at covered deck locations 4. Roofing Assembly a) Install roof rafter and cripple wall framing b) Install roof insulation c) Install plywood sheathing d) Install roofing membrane 5. Wall Assembly a) Install wall framing b) Install insulation c) Install interior gypsum board, finish and paint d) Install interior baseboard e) Install interior tile at bathroom locations f) Install interior doors g) Install exterior plywood sheathing h) Install exterior building wrap, flexible flashing and metal flashing, sill pans i) Install exterior siding j) Install exterior window and door assemblies 6. Electrical a) Install rough electrical b) Install electrical fixtures c) Install electrical panel and sub panel (for 2 story only) d) Install low voltage devices and rough ins-wires will be pulled in field e) Install conduit for Solar to roof (wiring and install of system in Owner Scope) f) Install conduit for EV Charger (wiring and install by Owner) (if applicable) 7. Plumbing a) Install rough plumbing-water, sanitary drain, gas b) Install water heater and outside and intake vent caps c) Install plumbing fixtures d) Install rough plumbing stub downs at floor and vent stub ups at roof 8. Mechanical a) Install mini splits b) Supply mechanical condenser -to be installed on site c) Install thermostats d) Install laundry room vent grill (if applicable) e) Install ERV and ERV grills/ducting f) Install ducting for bathrooms fans and hood vent g) Install Heat Mats and thermostats (if applicable) 9. Fire Sprinklers a) Install fire sprinkler manifold b) Install fire sprinkler heads, supply lines and stub downs c) Install fire sprinkler alarm bell d) Install fire sprinkler interior horn(s) 10. Appliances a) Install factory-installed appliances b) Install hood vent stub out 11. Casework a) Install casework b) Install countertops 12. Delivery Prep a) Install close-up plastic at all exterior walls for shipping b) Secure ship loose items c) Crb modules for truck pick up d) Provide forklifts as needed for loading modules onto trucks RESUME OF WORK FINISH INSTALLATION - IN FIELD SCOPE OF WORK 1. Structural Steel Frames a) Weld bottom steel corner plates and steel shim plates located at floor beams to steel weld plates on concrete stem wall and piers b) Weld mating side plates at modules' connection c) Install mate line bolts through roof beams at roof d) Install mate line connection plates through roof beams at roof e) Install bolts at storyline connections. (for 2 story only) 2. Floor Assembly a) Install plywood subfloor along floor mating seams b) Install insulation at floor mating seams c) Install wood flooring d) Complete stair landing assembly (for 2 story only) 3. Ceiling Assembly a) Install gypsum board ceiling, finish and paint at access blockouts (where applicable) b) Install mateline ceiling board between beams 4. Roofing Assembly a) Install mateline blocking as needed b) Install plywood sheathing along mating seams c) Complete roofing membrane mateline overlaps d) Install metal gutter and fascia trim metals e) Install metal downspouts f) Install metal trim piece at underside of blocking along roof beam mating seams g) Install roof ventilation 5. Wall Assembly a) Install gypsum board along wall mating seams and remaining areas, finish and paint b) Prime and paint along wall mating seams c) Install wall base along wall mating seams d) Install insulation along wall mating seams e) Install exterior plywood sheathing, flexible flashing lap and exterior furring strips along wall mating seams f) Install exterior siding along wall mating seams and remaining areas g) Install exterior metal corner caps/ exterior siding at corners (if applicable) h) Install exterior metal base fascia 6. Electrical a) Complete electric circuit and switch connections crossovers between modules b) Connect second floor subpanel to first floor subpanel (2 story only) c) Install remaining electrical fixtures d) Install exterior lights e) Test electrical systems in house 7. Plumbing a) Install roof vent sleeves and protection collars at vent stub ups b) Install remaining plumbing fixtures c) Test plumbing systems in house 8. Mechanical a) Install fan units b) Install supply and return air registers c) Complete thermostat wiring d) Install condenser f) Connect remaining ducting, including range hood and crossovers g) Test mechanical system 9. Appliances a) Install remaining appliances (within CH scope) b) Test appliances 10. Casework a) Install pre-assembled casework as needed at mating seams and in remaining areas RESUME OF WORK CONNECT HOMES - FACTORY NO SCALE 8 RESUME OF WORK CONNECT HOMES - FINISH INSTALLATION NO SCALE 7 <tr><td colspan="8"> 17085 MONTEBELLO RD </td></tr>								17085 MONTEBELLO RD MONTEBELLO RD							
17085 MONTEBELLO RD MONTEBELLO RD															

CONNECT HOMES[®]

706 S HILL ST. STE. 1060
LOS ANGELES, CA 90014
t: 310.622.9271
e: info@connect-homes.com

CONNECT 6: GRINSVEN RESIDENCE

17085 MONTEBELLO RD. CUPERTINO, CA 95014

DATE ISSUED

04.02.2021

APPROVING AUTHORITY

LICENSED ARCHITECT
JARED LEVY
C-33217
RENEWAL DATE
08/31/2021
STATE OF CALIFORNIA

MODEL HOME

3 BED / 2 BATH |
1,920 SF TOTAL

SHEET SET

STATE

SHEET TITLE

TITLE SHEET

SHEET, SHEET / MODEL,
SET, NUMBER, HOME

M-0.1
